POCMS · ETARIKHI/POCMS-PAYLOAD

Development progress report

Admin modernisation programme: retrospective, outlook and roadmap alignment

REPORTING DATE	PERIOD	BRANCH AND COMMIT	TIME ZONE
20 October 2026	1 to 20 Oct 2026	`1e75852c-pocms-payload` at `adff4e0`	Asia/Tehran (UTC+03:30)

SOURCES	EFFORT UNIT	PREPARED BY	STATUS
git history (80 commits), GitHub Actions (26 retained runs), repository docs, measurements taken for this report	Ideal engineer-days for one senior engineer, as in the roadmap	Arena agent (the programme's implementer), for the project owner	Measured facts, with estimates and forecasts labelled as such

Executive summary

EFFORT DELIVERED
81.1 eng-days
in 4 active days (16 Oct to 19 Oct); 41.1 on day one, median 11.5 per day since

ROADMAP P0–P6
82%
29 of 41 items delivered, 9 partial, 2 not started, 1 deferred

CURRENT ITERATION CR-12
7/12 items
12.0 of 26.0 eng-days (46%); planned work idle for 21 h

COMMITS
62 of 80
57 by the agent, 5 by the owner since 12 Oct; +23.3k / -4k authored lines

TESTS
99
51 integration and 48 end-to-end tests run today (6 visual on demand); baseline had 1 and 4 declared

CI PIPELINE
Red
since the revert on 19 Oct (prefix check); last green run `1238587` 19 Oct 08:00

ADMIN BUNDLE
+39.9 kB JS
27% of the +150 kB budget; CSS +19.2 kB (48% of +40); measured today

FORECAST
22 Oct
CR-12 complete, likely case (21 Oct to 23 Oct), if daily sessions resume on 21 Oct

DIMENSION	STATUS	ASSESSMENT
Scope	On track	The approved roadmap (P0–P6) is 82% delivered by effort: 29 of 41 items done, 9 partial, 2 not started. On top, the owner asked for the frontier-UI port and 15 change requests (three of them fixes); scope grew from 49.0 to 103.0 engineer-days.
Schedule	Ahead of plan	The roadmap planned 35–52 working days from 19 Oct (finishing between 4 Dec and 29 Dec). All seven phases landed on 16 Oct, before the planned start: about 10 weeks ahead of the upper-bound plan end.
Momentum	Slowing	No planned item has landed since 19 Oct 06:13 (21 h). The two sessions since then went to unplanned work: the Vercel build fix, its revert at the owner's request, and the Page speed fix (2.5 engineer-days, 0.5 of it reverted).
Quality	At risk	CI fails at the Tailwind prefix check since the revert, so integration and end-to-end tests don't run in CI. Locally all 51 integration tests pass; the dashboard, gallery and roles e2e suites pass, and the responsive suite fails on the overflow that the reverted fix `1238587` addressed. Failed CI runs are deleted from GitHub, so a pass rate can't be computed.
Performance	Within budget	`/admin` ships 685.1 kB JS and 64.4 kB CSS (compressed), measured today on a production build: 27% and 48% of the budgets. Two heavy builds were caught and rebuilt before they stayed: the first P5 build (899.5 kB, over budget) and the Recharts chart (787.2 kB, 95% of the budget).
Risk	Elevated	Highest risks: red CI (R1), no database migrations for production (R2), Preview builds without secrets (R3). Each has a concrete mitigation and two need an owner action.

Key messages

1. **Delivered.** In 4 active days the programme turned a stock, unbranded Payload admin into a themed, role-aware admin with a widget dashboard, TanStack lists, developer tools, a component gallery and four live integrations, documented in 11 ADRs and a guide.
2. **Velocity.** Measured with the roadmap's own estimates, 81.1 engineer-days of scope landed: 41.1 on 16 Oct (analysis and P0–P6), then 11.5, 9.0, 19.5 per day on change requests (median 11.5). This compares scope

against human-effort estimates; it is not a measure of hours worked.

3. **Momentum.** Throughput is high but the last 21 hours produced no planned scope. Rework is low over the whole programme (3% of effort) but concentrated on 19 Oct.
4. **Outlook.** 14.0 engineer-days remain in CR-12 (Jobs, Audit log, System page, Terminal, close-out), plus a 1.0-day migration baseline that the new collections need. Likely completion Thu 22 Oct (range 21 Oct to 23 Oct), gated by two owner actions.
5. **Alignment.** The work follows four of the roadmap's six principles fully and two partly (accessibility: no screen-reader pass and gates off while CI is red; Payload 4 portability: more custom views to re-check). 11 roadmap items are partial or not started (7.9 engineer-days).

> **Decisions needed from the owner**
>
> - **DEC**: re-apply the two CI fixes (`2b7cde3` , `1238587`) without the reverted build change, so CI runs the test suites again.
> - **ENV**: set PAYLOAD_SECRET and POSTGRES_URL for Vercel Preview, GOOGLE_API_KEY (both Google APIs enabled), VERCEL_TOKEN / VERCEL_PROJECT_ID, and CRON_SECRET for the jobs.
> - **MIG**: approve a baseline database migration and a `payload migrate` step before Jobs and Audit log add collections.
> - Confirm the Terminal page scope (development only, allow-listed scripts), and keep failed CI runs from now on so quality can be measured.


Contents

1. Retrospective: timeline, milestones, plan vs actual, velocity and momentum, engineering health
2. Prospective: current iteration, backlog and estimates, dependencies, forecast schedule
3. Strategic alignment: roadmap position, principles, guardrails, risks, trajectory
4. Appendix: method, roadmap item status, latest bundle measurement, commit register

1. Retrospective

The repository started on 1 Oct with the owner's foundation work: content model, seed data, analytics, GraphQL, the public site and email (18 commits to 12 Oct). The admin modernisation programme began with the analysis committed on 16 Oct 03:14 and ran in 11 working sessions to 19 Oct 23:47.


Figure 1. Project timeline, 1 to 20 October (day resolution)

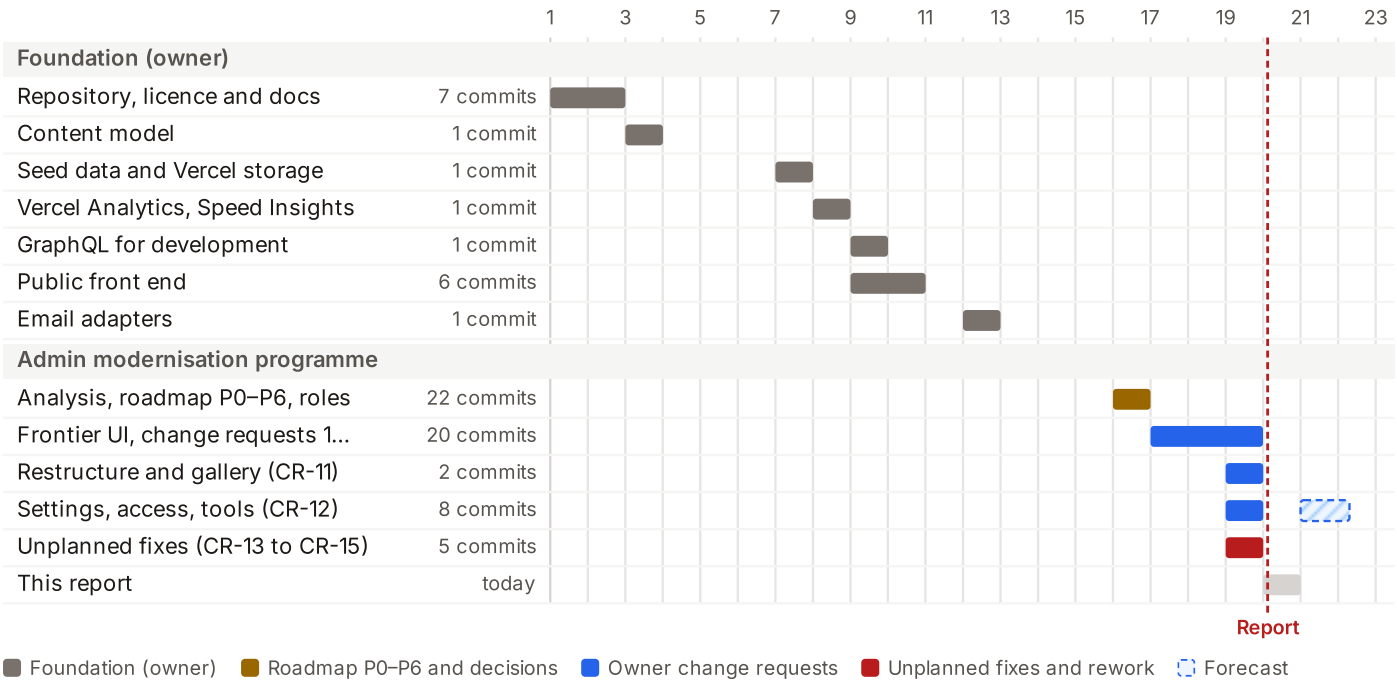

Bars span the calendar days with commits. The hatched bar is the likely forecast for the rest of CR-12. Days are counted in Asia/Tehran time.

1.1 Milestones and technical work

Figure 2. Programme timeline by hour, 16 to 20 October

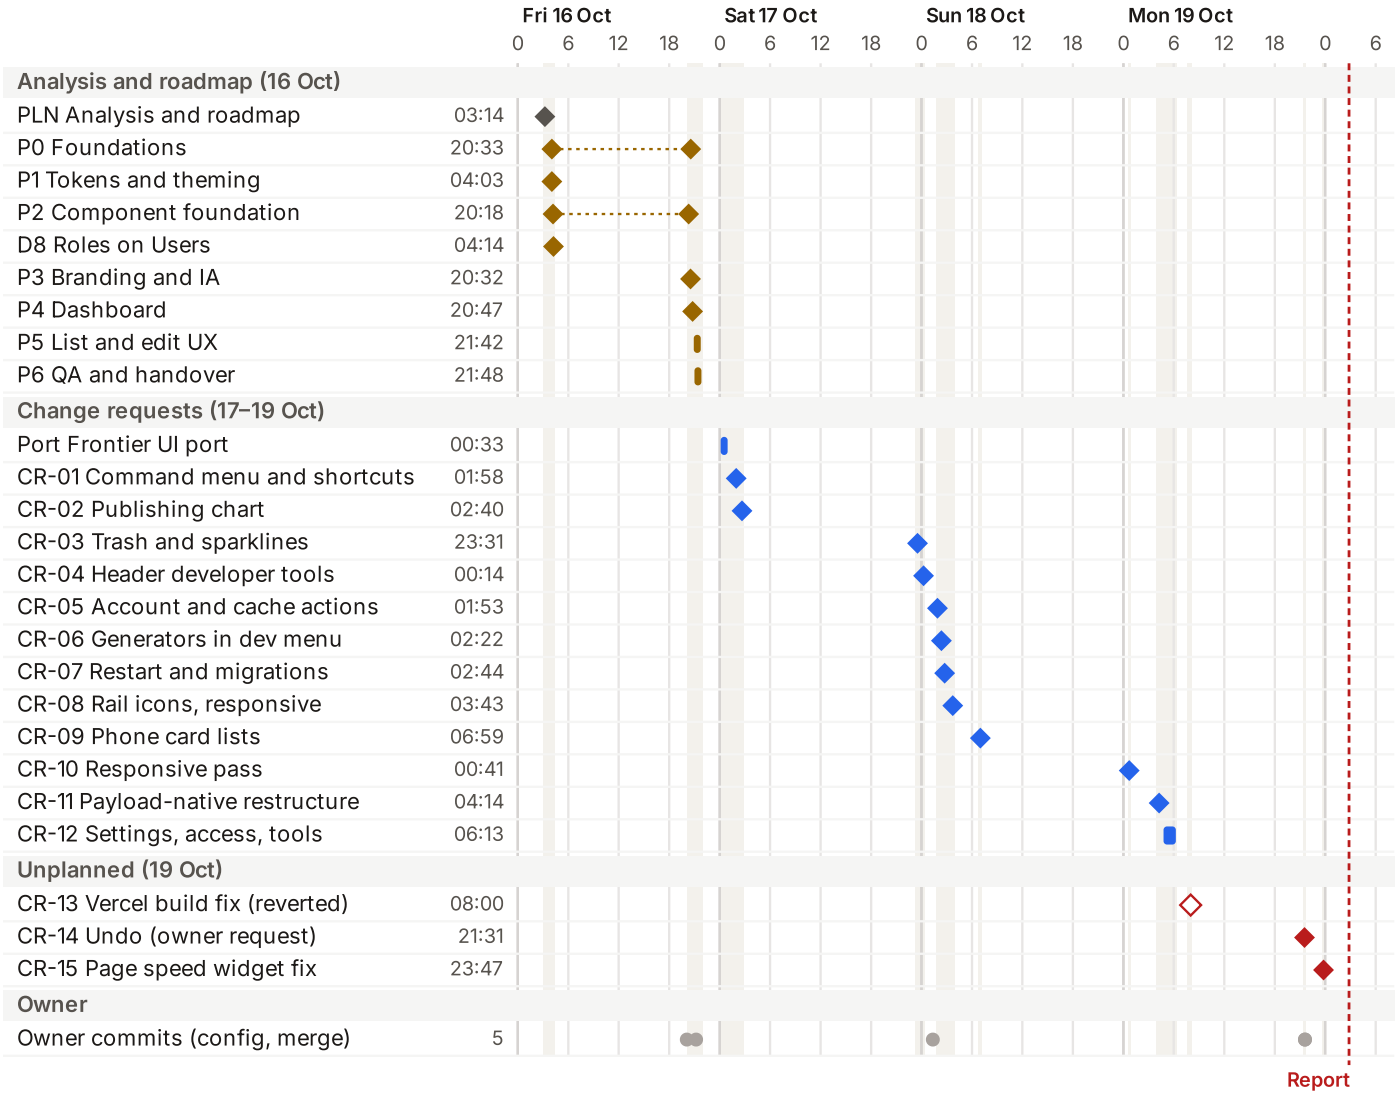

Bars run from a deliverable's first to its last commit; diamonds mark deliverables whose commits landed within 25 minutes; the hatched entry was reverted. Shaded columns are working sessions (agent commits less than 90 minutes apart). The right column of the label area is the landing time.

Commit times record when work was committed, not how long it took: a phase whose commits span 30 minutes may rest on hours of preparation. Durations here are therefore lower bounds of elapsed time, not effort.

ID	MILESTONE AND TECHNICAL WORK	LANDED	COMMITS	LINES (AUTHORED)	EFFORT (D)
PLN	**Admin UI analysis and phased roadmap** Audit of the stock admin, AdminCN and shadcnstudio study, Payload 3.90.2 capabilities checked in the packages, Payload 4 beta outlook; seven phases estimated at 35–52 engineer-days and eight decisions (D1–D8).	16 Oct 03:14	1	+1,014 / -0	4.0
P0	**P0 Foundations** Postgres 17 compose file and seed with real media; ESLint fixed (0 errors), typecheck and a CI workflow (lint, types, generated-file drift, contrast, int, build + e2e); 48 baseline screenshots; bundle baseline 645.2 kB JS / 45.2 kB CSS; ADRs 0001–0008.	16 Oct 20:33	7	+745 / -153	5.0
P1	**P1 Tokens and theming** Three-tier tokens (brand, Payload variables, semantic), self-hosted Inter, navy dark theme, AA primary (#996600 / #da9100), CI contrast check of 34 token pairs.	16 Oct 04:03	1	+315 / -19	5.0

ID	MILESTONE AND TECHNICAL WORK	LANDED	COMMITS	LINES (AUTHORED)	EFFORT (D)
P2	**P2 Component foundation** Isolated Tailwind v4 (acn: prefix, no Preflight, scoped scanning, layer order after Payload), 25 Base UI primitives, AST-based prefix checker in CI, living style guide with axe checks.	16 Oct 20:18	2	+4,042 / -50	5.5 of 6.0
D8	**D8 Roles on Users** Admin and editor roles saved to the JWT, no self-promotion, first user is an admin, lock-out protection; integration tests.	16 Oct 04:14	1	+205 / -4	1.5
P3	**P3 Branding and IA** Logo, icon and meta; sidebar groups; permission-aware Create menu; View site link; one-document collections (Header, About) that redirect to their document.	16 Oct 20:32	1	+554 / -79	3.2 of 4.0
P4	**P4 Dashboard** Server-component widgets on Payload's modular dashboard (Welcome, Content count, Publishing activity, Needs attention, Recent changes) using the Local API with access control; role-aware layout; axe in both themes.	16 Oct 20:47	1	+658 / -0	7.8 of 8.5
P5	**P5 List and edit UX** TanStack Table v9 lists with boolean, progress and colour cells; edit layouts; colour and icon tile pickers; media thumbnails; lazy islands brought /admin back from +254 kB to +21 kB JS.	16 Oct 21:42	3	+1,593 / -679	6.0 of 10.0
P6	**P6 QA and handover** Admin UI guide, README and docs index, AGENTS.md, 48 after-screenshots, unused packages removed, front-end fix for an unsaved Footer global.	16 Oct 21:48	5	+300 / -44	3.1 of 5.0
Port	**Frontier UI port** From three exploratory branches: sidebar icons with a collapsible icon rail, theme switch, cache refresh, article Live Preview, list summaries, 14 px body text.	17 Oct 00:33	3	+932 / -72	4.0
CR-01	**Command menu and shortcuts** Ctrl+K command menu loaded on demand (6.5 kB chunk), theme reveal animation, keyboard-shortcut layer with help and an off switch; budget raised to +150 / +40 kB.	17 Oct 01:58	3	+1,181 / -23	3.0
CR-02	**Interactive publishing chart** Range, series, tooltips and month drill-down; rebuilt without Recharts as an accessible radio-group plot (/admin 787.2 kB down to 680.1 kB).	17 Oct 02:40	3	+725 / -144	2.0
CR-03	**Trash and sparklines** Payload trash on eight collections: editors restore, only admins delete permanently; server-rendered sparklines on the count cards.	17 Oct 23:31	2	+433 / -7	2.5
CR-04	**Header developer tools** GraphQL Playground button and a developer tools menu in the header (REST JSON of the current view, access, session).	18 Oct 00:14	1	+303 / -11	1.5
CR-05	**Header account and cache actions** Account menu with log out, cache actions in the dev menu, one sidebar control (mobile menu, desktop rail), themed sidebar icon colours.	18 Oct 01:53	1	+529 / -261	1.5
CR-06	**Code generators in the dev menu** Types, import map, Drizzle schema, GraphQL schema and generate:all from the menu, in development only.	18 Oct 02:22	1	+238 / -5	1.0
CR-07	**Restart and migrations** Restart dev server, create migration, migration status, purge cached pages; menu items depend on the environment.	18 Oct 02:44	1	+538 / -159	1.5
CR-08	**Rail group icons, responsive layout** Group headings keep icons in the rail; saved views removed at the owner's request; phone and tablet layout for header, dashboard, lists and menus.	18 Oct 03:43	2	+357 / -77	2.0
CR-09	**Phone card lists** List rows become cards on phones, with thumbnails and selection.	18 Oct 06:59	2	+233 / -8	1.5
CR-10	**Responsive pass** Fluid type, menu sizing and touch targets across the admin.	19 Oct 00:41	1	+452 / -110	1.5
CR-11	**Payload-native restructure** Components laid out by Payload slot (ADR 0009); UI kit replaced by a component gallery; dashboard integrations research; bundle re-measured.	19 Oct 04:14	2	+1,806 / -1,357	4.0

ID	MILESTONE AND TECHNICAL WORK	LANDED	COMMITS	LINES (AUTHORED)	EFFORT (D)
CR-12	**Settings, access and admin tools** Site settings group, low-glare light canvas, Roles collection with access levels and capabilities, GraphQL document tab, and the Site traffic, Page speed, Deployments and CI status widgets.	19 Oct 06:13	8	+4,651 / -314	12.0 of 26.0
CR-13	**Vercel build fix (reverted)** Build no longer failed without PAYLOAD_SECRET / POSTGRES_URL; two CI fixes. Reverted the same day at the owner's request.	19 Oct 08:00	3	+102 / -13	~~0.5~~
CR-14	**Undo at the owner's request** Revert of CR-13. CI has been red since then (prefix check).	19 Oct 21:31	1	+13 / -102	0.0
CR-15	**Page speed widget fix** Lighthouse lab test through PageSpeed Insights streamed with Suspense and cached a day; CrUX fallback; Google errors explained with fix links; Referer header; 60 s function limit.	19 Oct 23:47	1	+1,346 / -277	2.0

Effort is the estimate in ideal engineer-days. Roadmap phases show the plan midpoint scaled by item completion ("of" gives the planned figure); CR-12 shows the seven finished items; the reverted build fix counts zero. Lines exclude generated files and lockfiles; renames count only changed lines.


Working sessions

	WINDOW (LOCAL TIME)	COMMITS	COMPLETED
1	16 Oct 03:14 to 04:14	9	PLN, P1, D8
2	16 Oct 20:18 to 21:48	13	P0, P2, P3, P4, P5, P6
3	17 Oct 00:08 to 02:40	9	Port, CR-01, CR-02
4	17 Oct 23:28 to 00:14	3	CR-03, CR-04
5	18 Oct 01:53 to 03:43	5	CR-05, CR-06, CR-07, CR-08
6	18 Oct 06:54 to 06:59	2	CR-09
7	19 Oct 00:41 to 00:41	1	CR-10
8	19 Oct 04:07 to 06:13	10	CR-11, CR-12
9	19 Oct 07:45 to 08:00	3	CR-13
10	19 Oct 21:31 to 21:31	1	CR-14
11	19 Oct 23:47 to 23:47	1	CR-15

1.2 Plan against actual


The roadmap estimated P0–P6 at 35–52 working days for one senior engineer, starting in the week of 19 Oct. All seven phases landed between 03:42 and 21:48 on 16 Oct, three days before the planned start. Scope coverage is the honest measure of that delivery: 27 items are done as planned, 2 were done differently for a stated reason, 9 are partial and 2 not started; the optional upgrade to 3.91 was not taken (the admin runs on 3.90.2).

Figure 3. Roadmap P0–P6: planned schedule against actual delivery

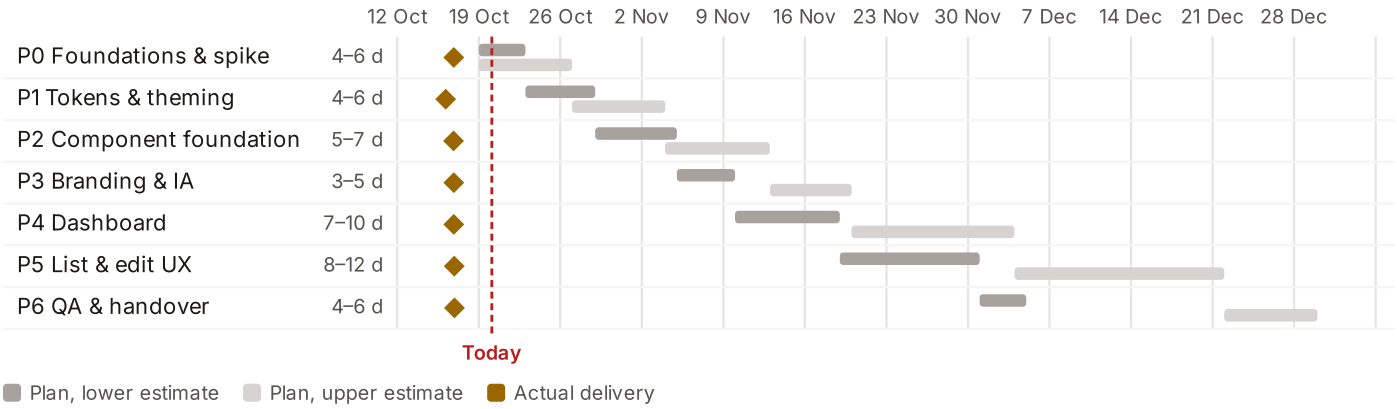

Planned schedule from the roadmap (§9.1): sequential phases from 19 October, weekends excluded, at the lower (dark) and upper (light) estimates, ending 4 Dec or 29 Dec. Diamonds: actual delivery.

Figure 4. Roadmap items by status and phase

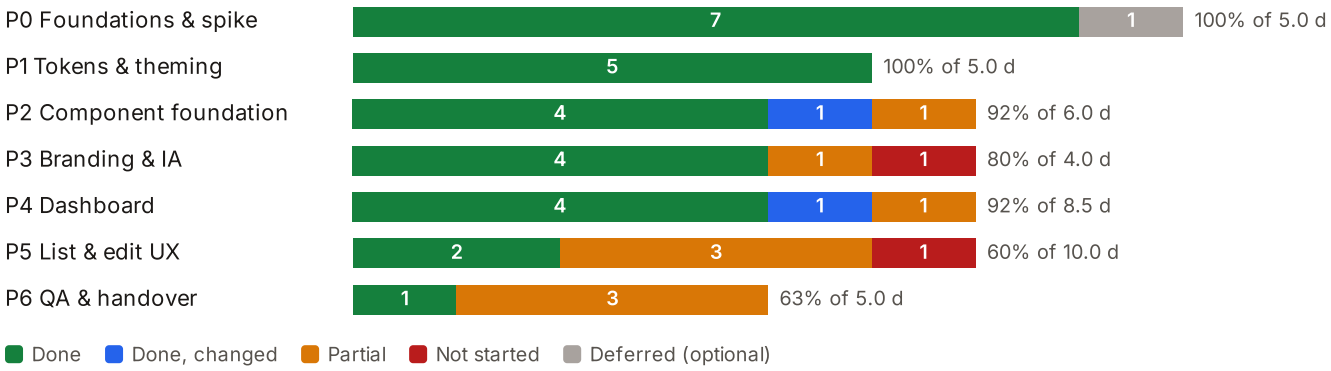

Counts of the 41 planned items. The percentage is the effort-weighted completion of the non-optional items (done or changed = 1, partial = 0.5) against the phase's planned midpoint: 35.6 of 43.5 engineer-days overall.


Open roadmap items

PHASE	ITEM	STATUS	EVIDENCE
P2	Component tests (Testing Library) and axe checks	Partial	axe in e2e; no component tests
P3	Resolve orphan SiteSettings / Navigation files	Not started	both files are still empty
P3	About / Header as globals (optional)	Partial	optional; Footer is a global, the others are one-document collections
P4	Role-aware defaultLayout, widget fields, i18n labels	Partial	no i18n labels
P5	Fields: colour picker, icon picker, image source	Partial	no ImageSourceField
P5	Media sizes, focal point, MIME types, thumbnails, regeneration script	Partial	thumbnail size and admin thumbnail only
P5	Drafts, live preview, orderable, command palette, SEO plugin (optional)	Partial	optional; live preview and command menu delivered
P5	Task-based acceptance tests against the baseline	Not started	feature e2e only
P6	Visual-regression suite in CI	Partial	suite exists (pnpm test:visual), not in CI
P6	axe suite, manual screen-reader pass, enforced budgets	Partial	axe in e2e; no SR pass; budget measured by hand
P6	Docs: guide, ADRs, AGENTS.md, README, changelog	Partial	no changelog

1.3 Velocity and momentum


Velocity is measured as estimated effort delivered per calendar day, using the roadmap's unit so planned and requested work are comparable. Day one carries the pre-analysed roadmap (41.1 engineer-days). From 17 Oct, when the work became owner-driven change requests, daily velocity was 11.5 (17 Oct), 9.0 (18 Oct), 19.5 (19 Oct): median 11.5, total 40.0. These three days are the basis of the forecasts.

Figure 5. Velocity: estimated effort delivered per day

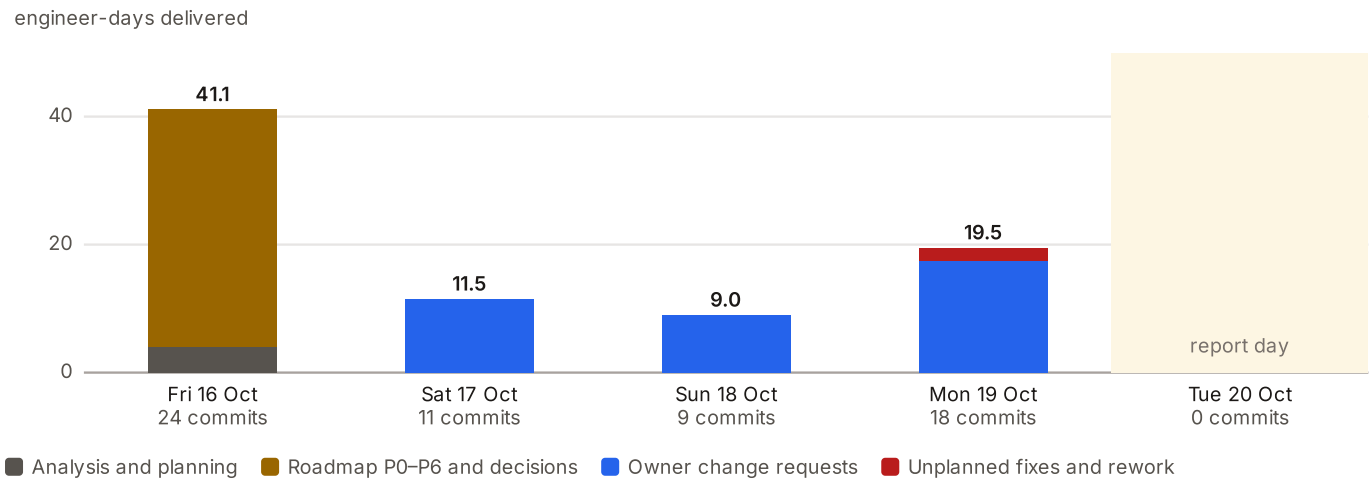

Each deliverable counts on the day of its last commit. 20 Oct is the report day (no code). On 19 Oct 2.0 of 19.5 engineer-days were unplanned; the reverted build fix (0.5) is not counted.

Figure 6. Burn-up: scope and delivered effort

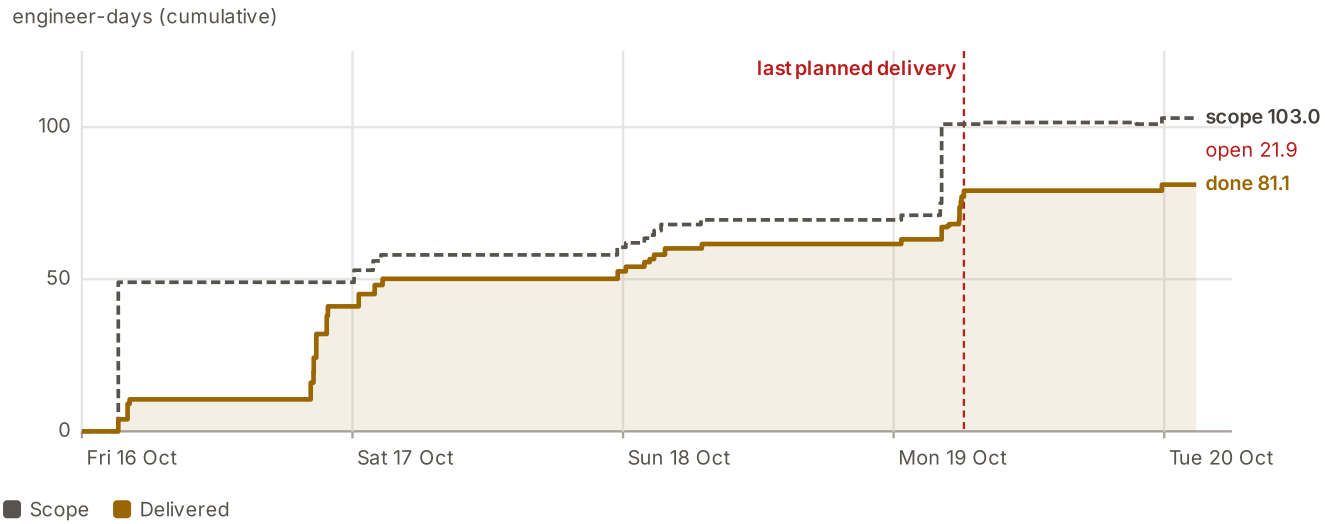

Scope starts with the analysis, the roadmap midpoint and decision D8 (49.0 engineer-days) and grows with each change request, CR-12 adding 26.0 at once. The gap at the right edge (21.9) is the open CR-12 work (14.0) plus the partial and open roadmap items (7.9).

> **Momentum reading.** Throughput rose again on 19 Oct (19.5 engineer-days), but all of its planned work (17.5) landed before 06:13. The next two sessions handled a production build failure, the owner's request to undo that fix, and a Page speed widget that did not work for the owner (fixed 19 Oct 23:47, about 18 h after it shipped). The pattern is a loss of flow on integration and deployment issues, not a drop in delivery capacity; restoring green CI and setting the Vercel variables removes its two causes.

Figure 7a. Commits per day by type, 1 to 20 October


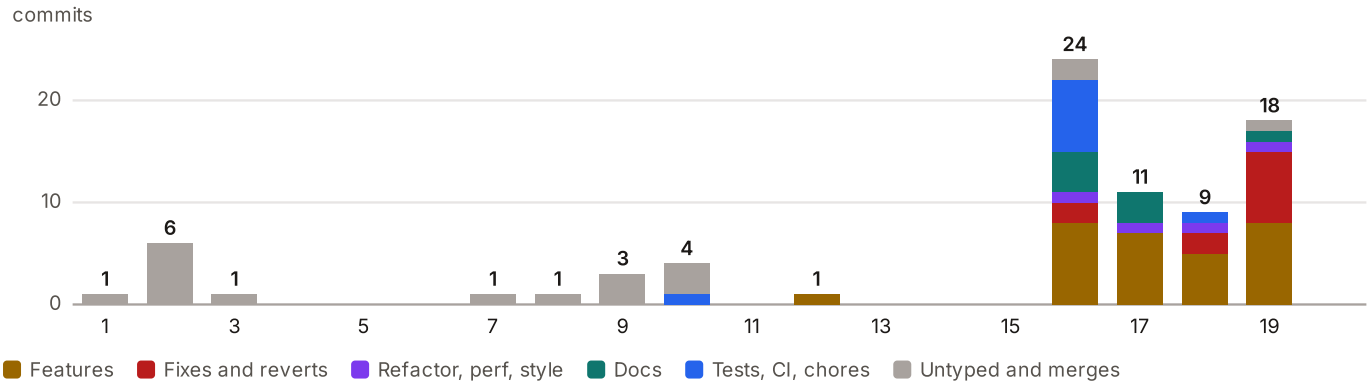



Figure 7b. Authored lines added (up) and deleted (down) per day

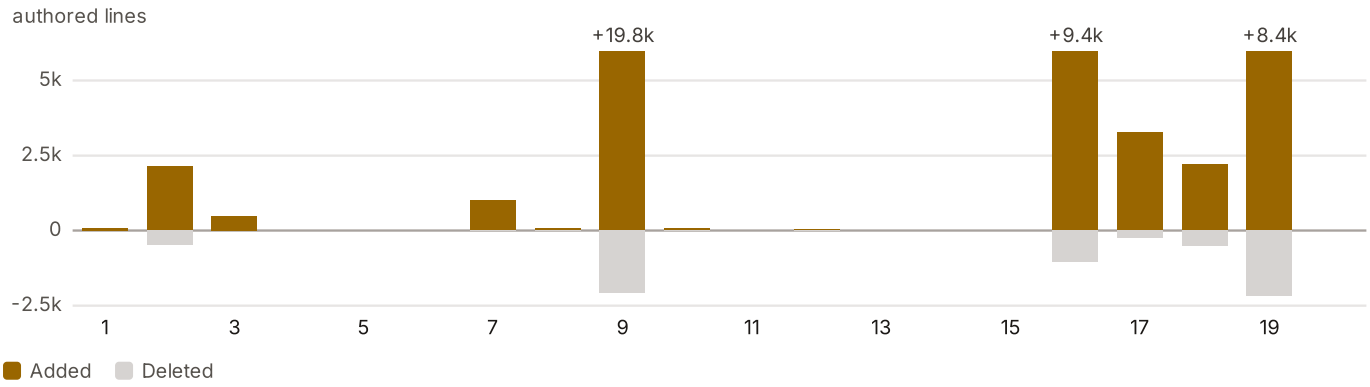

Generated files, lockfiles and binaries excluded; bars above 6,000 lines are cut and labelled. The 9 Oct spike is the owner's import of the public site; 16 Oct is the roadmap.


1.4 Engineering health

Figure 8. Test declarations over the programme

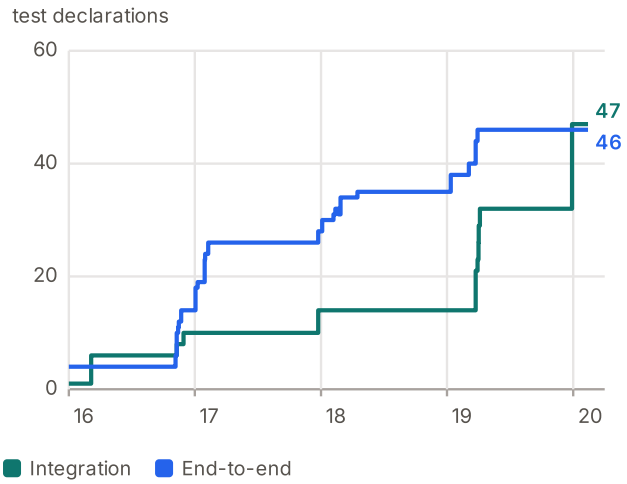

Static count of `test()` / `it()` declarations per commit. At run time the suites hold 51 integration tests in 7 files and 48 end-to-end tests in 13 files (some are generated in loops), plus 6 visual tests.

Figure 9. CI runs by run number

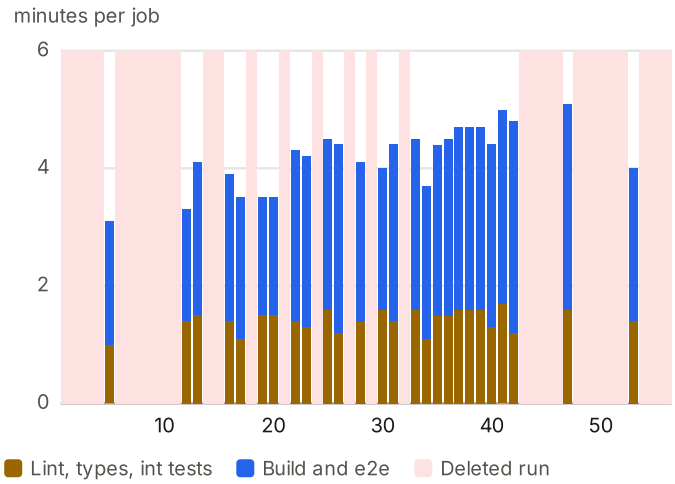

26 runs are retained, all successful (3.2 min at run 5, 5.4 min at the longest). Red columns are run numbers up to #53 that no longer exist (27), plus about three later runs; failed and cancelled runs were deleted. The last observed run (`adff4e0`) failed at the prefix check.

Figure 10a. JavaScript on /admin against the budget



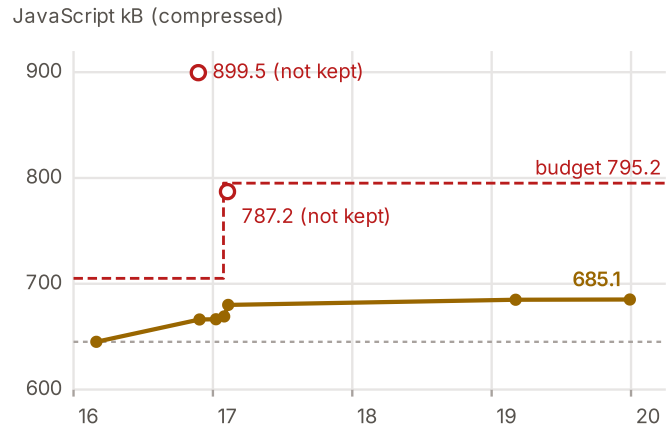


Figure 10b. CSS on /admin against the budget

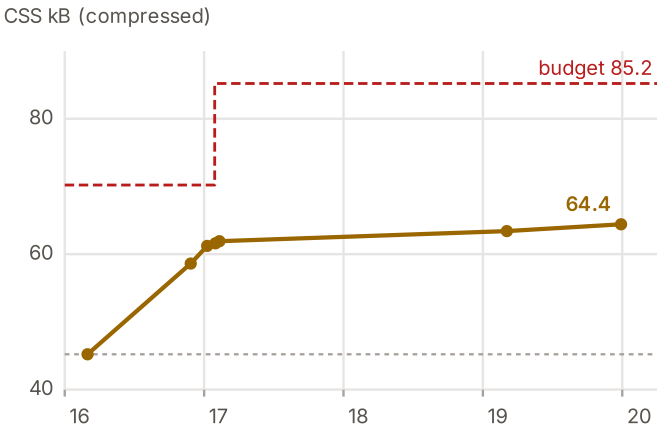


Compressed transfer size on a production build, logged in as an administrator (`scripts/measure-admin-bundle.mjs`). The budget was +60 kB JS / +25 kB CSS over the P0 baseline until the owner raised it to +150 / +40 on 17 Oct. Hollow red points were measured and rebuilt before they stayed: the first P5 build (899.5 kB, over the budget of the time) and the Recharts chart (787.2 kB, inside the raised budget but using 95% of it). Today's point was measured for this report at `adff4e0` .

Figure 11. Lines of code by area: 12 October baseline and today

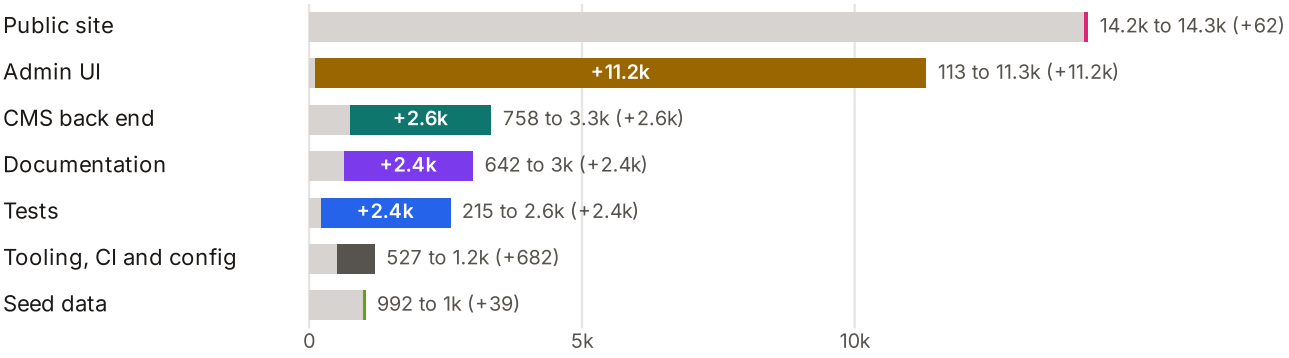


Text lines in tracked files at `0d7dde1` (grey) and `adff4e0` (growth in colour), generated files excluded (24.2k to 27.2k lines). Authored code grew from 17.5k to 36.8k lines; the admin from 113 to 11,311.

Figure 12. Authored lines changed by area, programme

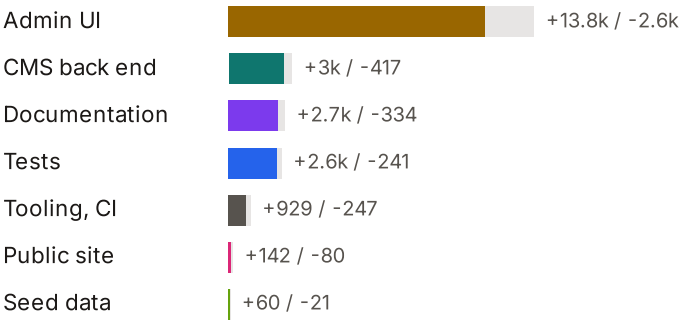

Added (colour) and deleted (grey) lines since the baseline, generated files excluded.

Figure 12b. Programme commits by type

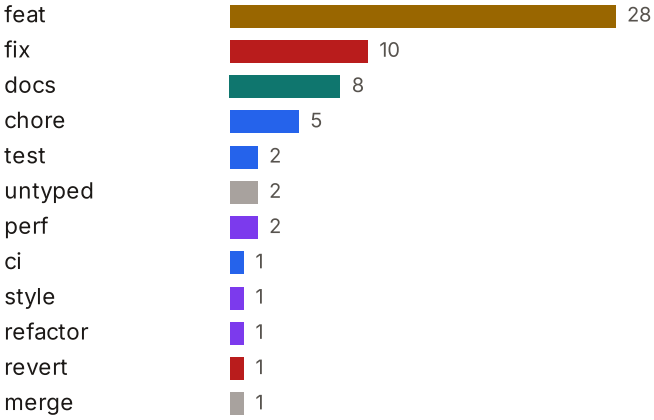


28 feature commits of 62; untyped commits are the owner's.

2. Prospective planning

The open work is the second half of CR-12 (admin tools E4–E7 and the close-out), two owner actions that unblock it, one enabling task found while preparing this report (database migrations), and the next horizons. Estimates are in ideal engineer-days; calendar dates follow from the observed velocity and assume daily sessions from Wed 21 Oct.

2.1 Current iteration: CR-12

Figure 13. CR-12 burn-down with forecast

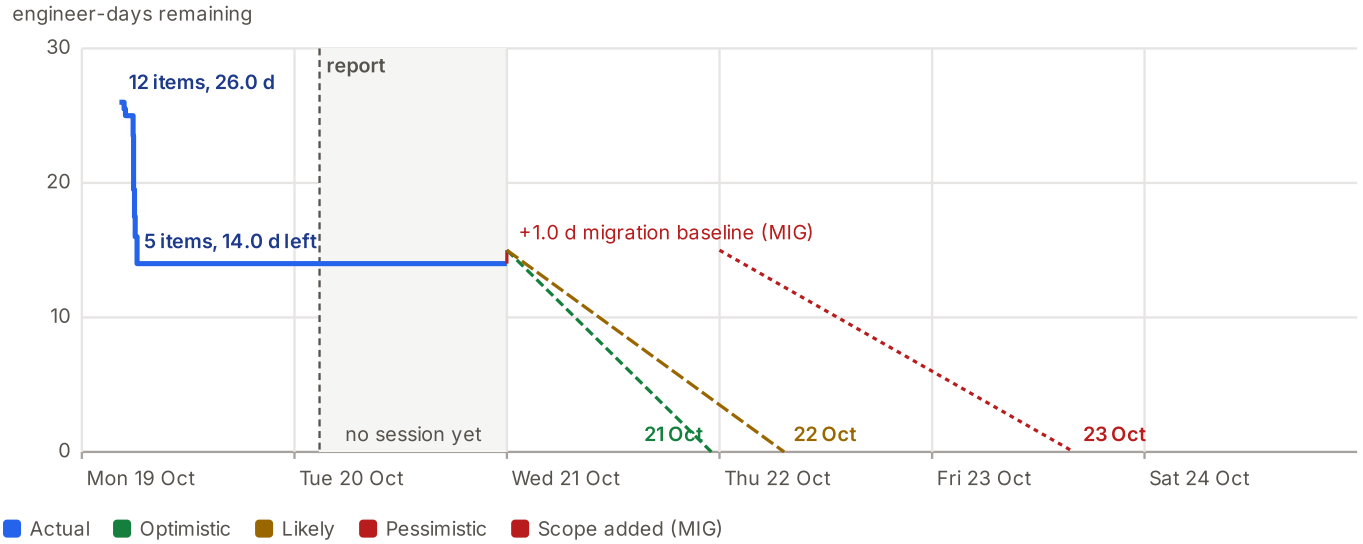

Actual: remaining effort after each finished item (A to E3 on 19 Oct). Forecasts start at the next session and use the highest (19.5), median (11.5) and lowest (9.0) observed daily velocity; the pessimistic case also waits one day for the owner decisions.

ITEM	SCOPE	ESTIMATE (D)	STATUS
A	Site settings group; Services under Profile	0.5	**Done** 04:46, `712a17c`
B	Low-glare light canvas (ADR 0010)	0.5	**Done** 04:56, `35bea29`
C	Roles, access levels, capabilities (ADR 0011)	4.0	**Done** 05:50, `90807ad` `c1ec5a8`
D	GraphQL tab wherever the API tab exists	1.5	**Done** 05:47, `1ebcdf5`
E1	Site traffic widget	2.0	**Done** 05:57, `419dec3`
E2	Page speed widget	1.5	**Done** 06:01, `7dcf315`
E3	Deployments and CI status widgets	2.0	**Done** 06:13, `a1fe7c8`
E4	Jobs panel, scheduled tasks, Page speed history	5.0	**Not started**
E5	Audit log	3.0	**Not started**
E6	System page	2.0	**Not started**

ITEM	SCOPE	ESTIMATE (D)	STATUS
E7	Terminal page (development only)	3.0	Not started
E8	Close-out: docs and bundle measurement	1.0	Not started


2.2 Backlog, estimates and scheduled deliverables

ID	TASK	EST. (D)	DEPENDS ON	LIKELY FINISH
DEC	**Decide on the two CI fixes** Re-apply 2b7cde3 (status tone renamed) and 1238587 (screen-reader text clipped) without the reverted build change. Restores green CI; until then lint passes but the prefix check stops the pipeline before tests run.	owner	–	21 Oct
ENV	**Vercel environment variables** PAYLOAD_SECRET and POSTGRES_URL for Preview builds; GOOGLE_API_KEY with both Google APIs enabled; VERCEL_TOKEN / VERCEL_PROJECT_ID; GITHUB_TOKEN if the repo turns private; CRON_SECRET for E4.	owner	–	21 Oct 21 Oct to 22 Oct
MIG	**Migration baseline and deploy step** There is no src/migrations: production gets schema changes only through a development-mode push. Roles, trash and widget changes already need it; E4 and E5 add collections. Create a baseline migration and run payload migrate during deployment.	1.0	DEC	21 Oct 21 Oct to 22 Oct
E4	**Jobs panel and scheduled tasks** maintenance queue run by Vercel Cron calling the jobs endpoints with a CRON_SECRET check (daily on Hobby); tasks: empty old trash (daily), PageSpeed run into a pagespeed-reports collection (daily), broken-link check (weekly); /admin/jobs with Run now and Cancel (manageJobs).	4.0	DEC, MIG, ENV	21 Oct 21 Oct to 23 Oct
E4b	**Page speed history** Lab score trend in the Page speed widget from stored runs; a Run again action using the pagespeed cache tag.	1.0	E4	21 Oct 21 Oct to 23 Oct
E5	**Audit log** afterChange / afterDelete hooks into an admin-only collection; filterable list and a dashboard widget (viewAuditLog capability).	3.0	DEC, MIG	21 Oct 21 Oct to 22 Oct
E6	**System page** Versions (commit, Node, Next, Payload), environment, which integrations are configured (never values), newer releases on npm (viewSystem).	2.0	DEC	21 Oct 21 Oct to 22 Oct
E7	**Terminal page** Development only, useTerminal capability, allow-listed package scripts with streamed output; reuses the environment detection of E6. Needs a short security review.	3.0	E6	22 Oct 21 Oct to 23 Oct
E8	**Docs and bundle close-out** Guide sections for the tools, perf-budget entry, gallery specimens.	1.0	E4b, E5, E7	22 Oct 21 Oct to 23 Oct
QA	**Roadmap gaps and quality gates** Visual suite and a bundle check in CI, changelog, component tests, task-based acceptance tests, orphan globals resolved, screen-reader pass (needs a person).	6.0	DEC	22 Oct 22 Oct to 24 Oct
CNT	**Content and publishing** Drafts and versions with scheduled publishing (runs on the jobs queue from E4), SEO plugin, admin i18n labels, SiteSettings and Navigation globals, media size regeneration, list group-by.	10.0	E4, QA	23 Oct 22 Oct to 25 Oct
P7	**Payload 4 migration** Codemod, tokens re-pointed to v4 semantic tokens, payload-overrides.css deleted, list view and custom views re-checked. The visual suite in CI is the safety net.	10.0	QA Payload 4 stable (4.0.0-beta.1 on 2026-10-13)	not scheduled

Likely finish: median velocity from 21 Oct; second line: optimistic to pessimistic. Owner steps are assumed to take up to half a day and run alongside engineering. P7 waits for a stable Payload 4.

2.3 Dependencies

Figure 14. Dependencies of the remaining work

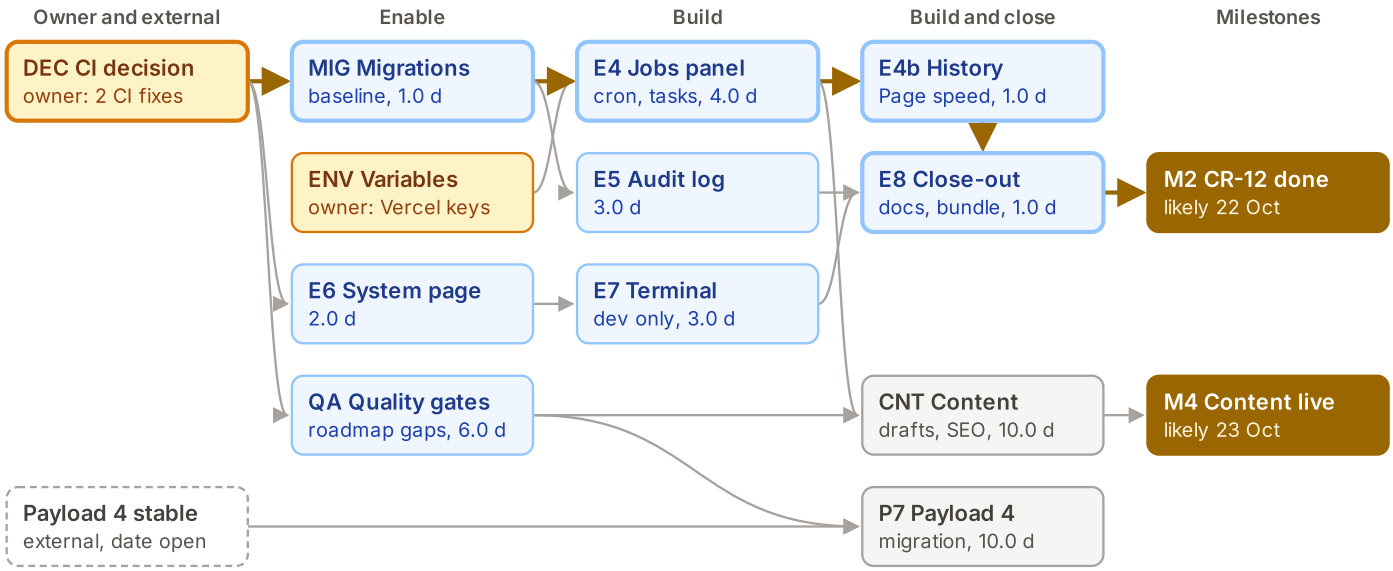


Arrows point from a prerequisite to the work it enables. The amber path is the critical path to closing CR-12: the CI decision, the migration baseline, the jobs queue (which the Page speed history and the later scheduled publishing both need), then the close-out.

- **Jobs before scheduling.** Payload's scheduled publish creates jobs and never runs without a job runner [1], so E4 is also a prerequisite of the content release. On Vercel the runner is a cron call to Payload's jobs endpoints, protected by CRON_SECRET; on the Hobby plan each cron job runs at most once a day, within the hour [2], which suits daily and weekly maintenance.
- **Migrations before new collections.** There is no `src/migrations`; production receives schema changes only through a development-mode push. Roles, trash and dashboard changes already depend on it, and E4/E5 add collections.
- **Terminal after System page.** Both need the same environment detection and capability gating; the Terminal also needs a short security review.
- **Payload 4 after quality gates.** The visual-regression suite in CI is the safety net for the token re-mapping in P7.

2.4 Forecast schedule

Figure 15. Forecast schedule (likely case, with range)

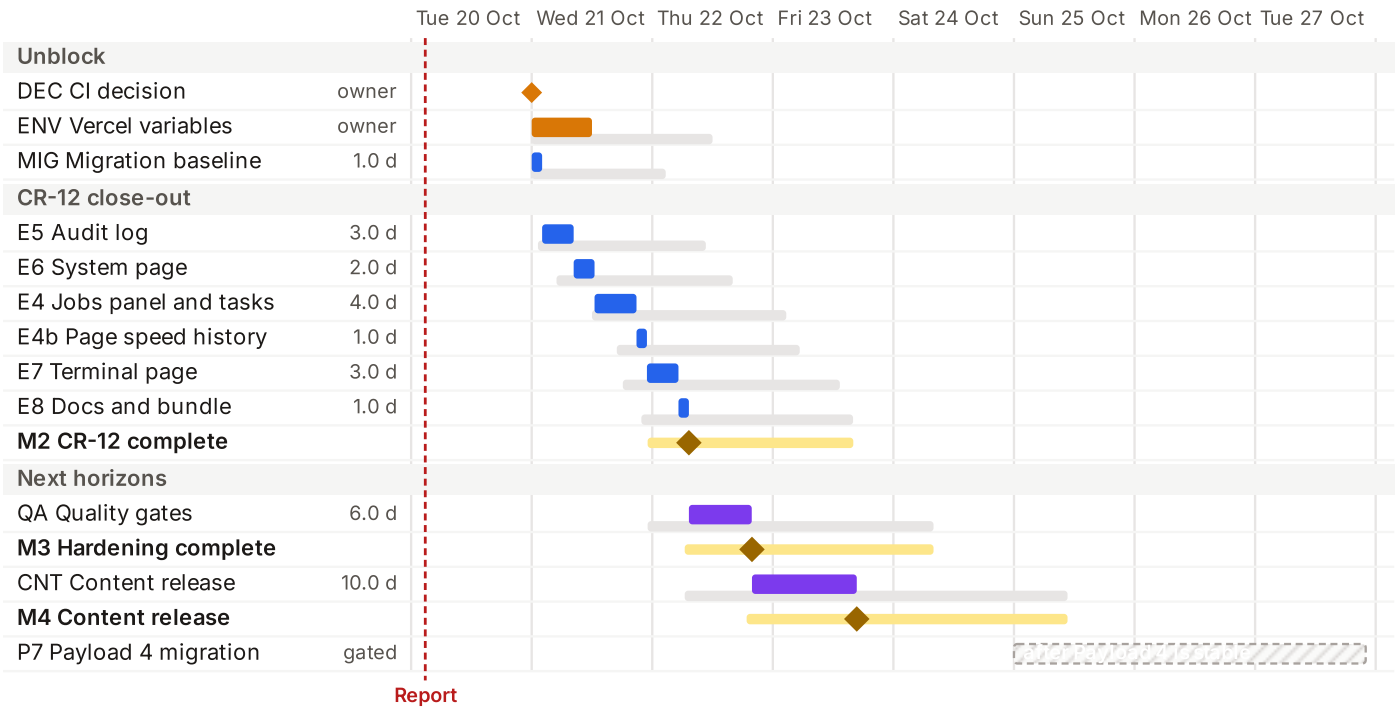

Coloured bars: likely schedule. Grey whiskers: from the optimistic start to the pessimistic finish. Diamonds: milestones at their likely date, the amber band shows their range.

ID	SCHEDULED DELIVERABLE	LIKELY	RANGE	BASIS
M1	CI green again	**Wed 21 Oct**	21 Oct to 22 Oct	Owner decision DEC, then re-apply two fixes
M2	CR-12 complete (E4–E8)	**Thu 22 Oct**	21 Oct to 23 Oct	15.0 engineer-days incl. the migration baseline
M3	Roadmap gaps closed, quality gates in CI	**Thu 22 Oct**	22 Oct to 24 Oct	Visual suite, bundle check, changelog, tests
M4	Content and publishing release	**Fri 23 Oct**	22 Oct to 25 Oct	If the owner schedules it next: drafts, scheduling, SEO, i18n, globals

Forecast assumptions. Sessions continue daily, as on 16–19 October, and the remaining items resemble the CR phase in size and risk. Velocity is measured on only three days, so the range is wide and should be re-based after the next session. Owner availability for the two decisions is the largest single factor; each day of delay moves every date by a day.

3. Strategic alignment


The long-term roadmap runs from the foundation through the P0–P6 modernisation to operations tooling, hardening, content capabilities and finally Payload 4 (P7, after v4 is stable). The programme sits in horizon H3: operations and governance, 46% of its estimated effort done.

Figure 16. Long-term roadmap and current position



H0–H2 are complete. H3 is in progress (CR-12). H4–H6 are planned; H6 depends on the Payload 4 release.

Figure 17. Remaining estimated effort by horizon



About 41.0 engineer-days remain across H3–H6, roughly 3.6 active days at the median velocity; H6 cannot start before Payload 4 is stable.


3.1 Alignment with the roadmap's guiding principles

PRINCIPLE (§8.1)	RATING	EVIDENCE
Payload owns the shell	Aligned	Native dashboard, list/edit slots and custom views; components laid out by Payload slot (ADR 0009). TanStack lists are the one owner-approved replacement of a core view (D7).
One source of truth for tokens	Aligned	tokens.css tiers feed Payload, components and Tailwind; contrast of every pair checked in CI; ADR 0010 canvas set in one place.
Additive and reversible	Aligned	All changes go through config and extension points. The 19 Oct revert of three commits applied cleanly.
Server-first	Aligned	Widgets and integrations are server components (secrets stay on the server); sparklines are server SVG; Page speed streams with Suspense. JS on /admin +39.9 kB in total.
Accessible by default (WCAG 2.2 AA)	Partly aligned	axe checks in e2e for dashboard, gallery, menus and roles in both themes; token contrast in CI. Missing: manual screen-reader pass. With CI red, the gates don't run.
Portable to Payload 4	Partly aligned	Token map and readiness checklist (ADR 0006); overrides kept in one file. Custom list view, document tab and views add re-check work for P7.

3.2 Guardrails

Admin JS budget		+39.9 of +150 kB (27%); 110.1 kB of headroom for E4–E7 and beyond
Admin CSS budget		+19.2 of +40 kB (48%); grows about 1 kB per feature set
Roadmap effort delivered		35.6 of 43.5 engineer-days (82%)
CR-12 effort delivered		12.0 of 26.0 engineer-days (46%)
CI duration		4.1 min at the last retained run against 3.2 min at run 5 (marker), as the suites grew; well inside the 20 / 30 min job limits
Quality gates in CI		8 of 11 gates are in CI: lint, types, generated files, contrast, prefix, integration tests, build, e2e with axe. Missing: visual suite and bundle budget (planned in P6), a migration check (recommended here). While CI is red, nothing after the prefix check runs.

3.3 Risks

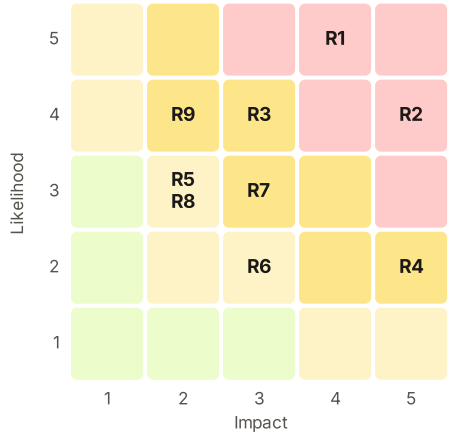

Likelihood and impact on a 1–5 scale; score = product.

ID	RISK	L	I	SCORE	MITIGATION
R1	CI stays red after the revert	5	4	20	Owner decision DEC; until then, run the suites locally before each push.
R2	Production schema drift (no migrations)	4	5	20	MIG before E4/E5: baseline migration, payload migrate in the deploy step.
R3	Preview builds fail without PAYLOAD_SECRET	4	3	12	Set the variables for Preview (ENV); the code guard stays reverted.
R4	Terminal page widens the attack surface	2	5	10	Development only, allow-list, capability check, security review before merge.
R7	Payload 4 timing and rework	3	3	9	Readiness checklist; visual suite in CI before P7; stay on 3.9x until v4 is stable.
R9	Lost CI history weakens traceability	4	2	8	Keep failed and cancelled runs (or export results) so pass rates can be measured.
R5	Integration widgets misconfigured	3	2	6	Widgets explain missing keys and Google errors with fix links (adff4e0).
R6	Bundle creep from new admin views	2	3	6	Server components and next/dynamic; 110 kB JS headroom; add a CI bundle check (QA).

ID	RISK	L	I	SCORE	MITIGATION
R8	Upstream bug: media folders with trash	3	2	6	Folders not enabled; tracked in payloadcms/payload#16327.

3.4 Trajectory

Measured against the original plan, the project is far ahead: everything estimated at 35–52 engineer-days is in place, the owner has added and received about 38.0 engineer-days of further scope, and the admin stays inside its performance budget with room to spare. Against its own recent pace the trajectory has flattened: delivery of planned scope paused while integration and deployment problems were handled, and the safety net (CI) is off.

The path back to full speed is short and concrete: the CI decision and the Vercel variables (owner), the migration baseline, then the jobs queue that unlocks three later features. On the median velocity CR-12 closes Thu 22 Oct, hardening Thu 22 Oct, and the content release Fri 23 Oct. Payload 4 remains the one item outside the project's control; the readiness checklist and a visual suite in CI keep that migration a contained step when it comes.

Appendix

A. Method and definitions

- **Commits and lines** come from `git log -M --numstat` on `arena/1e75852c-pocms-payload` at `adff4e0`. Authored lines exclude generated files (`pnpm-lock.yaml`, `schema.graphql`, `payload-types.ts`, `payload-generated-schema.ts`, `importMap.js`, `nav-icons.css`), lockfiles and binaries. Renames count only changed lines. Areas are assigned by path (see `scripts/progress-report/collect.mjs`).
- **Time**: commits are placed at their committer time and bucketed into calendar days in Asia/Tehran (UTC+03:30). Agent commits carry UTC timestamps, the owner's +03:30; the report uses the same zone for both.
- **Origin**: commits with UTC author and committer times are the agent's; the rest are the owner's (all commits use the owner's git identity).
- **Effort and velocity**: ideal engineer-days for one senior engineer. Roadmap phases use the midpoint of the plan's range, scaled by the completion of their non-optional items (done or changed = 1, partial = 0.5, not started = 0). Other deliverables carry the author's estimate on the same scale (milestone table in §1.1). These estimates are the implementer's own and have not been reviewed independently. Velocity is effort delivered per calendar day; it measures scope against human-effort estimates, not time spent.
- **Forecasts** schedule the backlog sequentially in dependency order at the highest, median and lowest observed daily velocity since 17 October, starting 21 Oct; the pessimistic case adds one day for owner decisions. They are estimates, not commitments.
- **Tests**: per-commit counts are static declarations (`git grep` for `test(` / `it(` under `tests/`); today's run-time counts come from the test runners (`vitest`, `playwright test --list`).
- **CI**: GitHub keeps 26 runs for this branch, all successful. Run numbers show that 27 runs up to #53 and about three later ones were deleted, so no pass rate is reported. The current red state is from the last observed run.
- **Bundle**: compressed transfer sizes from `scripts/measure-admin-bundle.mjs` against a production build; history from `docs/ui-modernization/perf-budget.md`, today's values measured for this report.

B. Reproducing this report

`node scripts/progress-report/build.mjs --pdf` regenerates the HTML, the PDF and `2026-10-20-progress-data.json` from git, `gh` and `scripts/progress-report/model.mjs` (plan, statuses, estimates, backlog, risks). Every number in the report is in the JSON file.

C. Roadmap item status (41 items)

	ITEM	STATUS	EVIDENCE
P0.1	Postgres dev environment, committed .env.example, seed	Done	c65bc55
P0.2	Quality baseline: ESLint, typecheck, int/e2e green, CI workflow	Done	daf243e, d430e6e
P0.3	Visual baseline: 48 screenshots, light/dark, 1440/768/375 px	Done	daf243e
P0.4	Bundle and CSS baseline (Playwright transfer sizes, not bundle-analyzer)	Done	2f87cb0
P0.5	Dependency audit: unused packages removed	Done	cccdf04
P0.6	Tailwind isolation spike (layers, scanning, .table, rem, portals, dark variant)	Done	7414431, ADR 0002
P0.7	Bump to Payload 3.91 and a v4 beta smoke test (optional)	Deferred (optional)	optional; still 3.90.2
P0.8	ADRs for decisions D1–D8	Done	2f87cb0
P1.1	tokens.css: three tiers, light/dark, status tokens	Done	b3f6f63
P1.2	Payload-native overrides: radius, Inter, navy dark theme, primary button	Done	b3f6f63
P1.3	Automated contrast check of every token pair, in CI	Done	check:contrast
P1.4	Visual review of core surfaces in both themes	Done	screenshots/p6-after
P1.5	v3 to v4 token map documented	Done	admin-ui-guide § Payload 4 readiness
P2.1	Tailwind v4, Base UI, cva, tw-animate-css installed; PostCSS config	Done	7414431
P2.2	components.json and shadcn registries	Done, changed	added in 7414431, retired by ADR 0009
P2.3	Primitive set reconciled with the tokens	Done	25 primitives
P2.4	AdminUIProvider registered as an admin provider	Done	b3f6f63
P2.5	Living style guide (/admin/ui-kit, now /admin/gallery)	Done	1eb40e7, d9ba8a3
P2.6	Component tests (Testing Library) and axe checks	Partial	axe in e2e; no component tests
P3.1	Logo, icon and admin.meta	Done	364f38c

	ITEM	STATUS	EVIDENCE
P3.2	admin.group mapping, descriptions, useAsTitle/defaultColumns audit	Done	364f38c
P3.3	Nav slots: Create menu, View site, style-guide link	Done	364f38c
P3.4	Resolve orphan SiteSettings / Navigation files	Not started	both files are still empty
P3.5	About / Header as globals (optional)	Partial	optional; Footer is a global, the others are one-document collections
P3.6	e2e tests for groups and branding	Done	navigation.e2e
P4.1	Query layer through the Local API with req and overrideAccess: false	Done	51945f8
P4.2	Six widgets (KPIs, health, activity, recent changes, quick actions)	Done	51945f8
P4.3	Chart island (planned with Recharts)	Done, changed	own accessible chart, about 107 kB less
P4.4	Empty, loading and error states	Done	all widgets
P4.5	Role-aware defaultLayout, widget fields, i18n labels	Partial	no i18n labels
P4.6	e2e (widgets, edit mode) and axe	Done	dashboard.e2e
P5.1	Cells: thumbnail, status, colour, icon, proficiency, relative date	Done	961da3a, 3b950c2
P5.2	Fields: colour picker, icon picker, image source	Partial	no ImageSourceField
P5.3	Edit layouts: tabs, rows, sidebar, descriptions, conditions	Done	3b950c2
P5.4	Media sizes, focal point, MIME types, thumbnails, regeneration script	Partial	thumbnail size and admin thumbnail only
P5.5	Drafts, live preview, orderable, command palette, SEO plugin (optional)	Partial	optional; live preview and command menu delivered
P5.6	Task-based acceptance tests against the baseline	Not started	feature e2e only
P6.1	Visual-regression suite in CI	Partial	suite exists (pnpm test:visual), not in CI
P6.2	axe suite, manual screen-reader pass, enforced budgets	Partial	axe in e2e; no SR pass; budget measured by hand
P6.3	Docs: guide, ADRs, AGENTS.md, README, changelog	Partial	no changelog
P6.4	Payload 4 readiness checklist	Done	ADR 0006, admin-ui-guide

D. Latest bundle measurement (adff4e0, 20 Oct)

ROUTE	JS FILES	JS KB	JS DECODED	CSS FILES	CSS KB	CSS DECODED
`/admin/login`	14	674.6	2275.7	7	64.4	438.6
`/admin`	16	685.1	2305.2	7	64.4	438.6
`/admin/collections/articles`	16	684.7	2307.6	7	64.4	438.6
`/admin/collections/articles/create`	15	674.9	2275.9	7	64.4	438.6
`/admin/gallery (admins only)`	22	798.5	2672.3	7	64.4	438.6

E. Commit register: programme (62 commits)

LANDED (LOCAL)	COMMIT	ORIGIN	TYPE	SUBJECT	LINES
16 Oct 03:14	`19e6c2c`	agent	docs	docs(ui): add shadcn/ui x Payload admin UI modernization analysis	+1,014 / -0
16 Oct 03:42	`c65bc55`	agent	chore	chore(dev-env): Postgres docker-compose, committed .env.example, offline seed with real media	+168 / -74
16 Oct 03:49	`daf243e`	agent	chore	chore(quality): working ESLint flat config, typecheck script, CI workflow, visual baseline	+264 / -60
16 Oct 03:55	`2f87cb0`	agent	docs	docs(adr): record decisions D1-D8; admin bundle baseline and budget	+254 / -0
16 Oct 03:56	`4b0e761`	agent	ci	ci: use current action majors (pnpm/action-setup v6 supports pnpm 11; node24 runtimes)	+7 / -7
16 Oct 04:03	`b3f6f63`	agent	feat	feat(admin-theme): design tokens, Inter, navy dark theme and brand primary for Payload's UI (P1)	+315 / -19
16 Oct 04:03	`5a2935f`	agent	test	test(visual): const for the document id map (fixes the CI lint error)	+1 / -1
16 Oct 04:11	`7414431`	agent	feat	feat(admin-ui): isolated Tailwind v4 with the acn prefix and Base UI primitives (P2)	+3,015 / -5
16 Oct 04:14	`72f69d0`	agent	feat	feat(auth): admin and editor roles on Users, with lock-out protection (D8)	+205 / -4

LANDED (LOCAL)	COMMIT	ORIGIN	TYPE	SUBJECT	LINES
16 Oct 20:05	`3ad199d`	owner	untyped	Run Time Changes	+2 / -7
16 Oct 20:18	`d430e6e`	agent	fix	fix(codegen): deterministic generated files; CI checks types, Drizzle schema, GraphQL and import map	+48 / -11
16 Oct 20:18	`1eb40e7`	agent	feat	feat(admin-ui): living style guide at /admin/ui-kit, initials avatar, shared tooltip delay	+1,027 / -45
16 Oct 20:32	`364f38c`	agent	feat	feat(admin-ia): PoCMS branding, grouped sidebar, Create menu and one-document collections (P3)	+554 / -79
16 Oct 20:33	`d94daf8`	agent	test	test(int): run integration files one at a time	+3 / -0
16 Oct 20:47	`51945f8`	agent	feat	feat(admin-dashboard): widgets on Payload's modular dashboard (P4)	+658 / -0
16 Oct 20:55	`961da3a`	agent	feat	feat(admin-lists): TanStack Table v9 list views, boolean/progress/color cells (P5, D7)	+413 / -5
16 Oct 21:00	`c48232a`	agent	docs	docs(admin-ui): admin UI guide (architecture, tokens, Tailwind prefix, widgets, lists, roles)	+209 / -0
16 Oct 21:00	`cccdf04`	agent	chore	chore(deps): remove unused packages	+0 / -27
16 Oct 21:11	`9e84aec`	owner	untyped	prevent stashes	+1 / -0
16 Oct 21:22	`3b950c2`	agent	feat	feat(admin-edit): edit layouts, tile pickers, media thumbnails and readable file sizes	+345 / -37
16 Oct 21:42	`2d0d1db`	agent	perf	perf(admin): back within the bundle budget (/admin +21 kB JS vs +254 kB before)	+835 / -637
16 Oct 21:46	`f1caab0`	agent	docs	docs: after screenshots, README and docs index for the admin UI, AGENTS.md (P6)	+57 / -4
16 Oct 21:48	`ec54913`	agent	fix	fix(frontend): home page renders before the Footer global is first saved	+34 / -8
16 Oct 21:48	`e73fe4d`	agent	chore	chore(pnpm): drop onlyBuiltDependencies from pnpm-workspace.yaml	+0 / -5
17 Oct 00:08	`2d8383c`	agent	feat	feat(admin-shell): sidebar icons with a collapsible icon rail, theme switch, cache refresh, article Live Preview	+669 / -49
17 Oct 00:30	`76c2e02`	agent	feat	feat(admin): list summaries, 14px body text, header actions in the UI kit	+244 / -23
17 Oct 00:33	`df5ad98`	agent	docs	docs(perf): bundle measurement after the admin shell (JS +0.2 kB, CSS +2.6 kB; within budget)	+19 / -0
17 Oct 01:50	`9609da6`	agent	feat	feat(admin): command menu (Ctrl+K), theme reveal animation, raised bundle budget	+916 / -16
17 Oct 01:56	`df2ce9b`	agent	feat	feat(admin): keyboard shortcuts layer with help dialog and an off switch	+250 / -7
17 Oct 01:58	`1010b73`	agent	docs	docs(perf): measurement after the command menu (/admin JS +2.7 kB, menu chunk 6.5 kB on demand)	+15 / -0
17 Oct 02:31	`2f2dd53`	agent	feat	feat(dashboard): interactive publishing chart (range, series, tooltips, month drill-down)	+535 / -46
17 Oct 02:38	`d60615b`	agent	perf	perf(dashboard): publishing chart without Recharts (accessible radio-group plot)	+174 / -98
17 Oct 02:40	`5fae69a`	agent	docs	docs(perf): measurement after the interactive chart (dashboard 680.1 kB; the Recharts version was 787.2 kB)	+16 / -0
17 Oct 23:28	`463a21c`	agent	feat	feat(admin): trash with restore (editors) and permanent delete (admins), saved list views	+355 / -3
17 Oct 23:31	`7ffebf7`	agent	feat	feat(dashboard): sparklines of monthly additions on the count cards (server-rendered SVG, no client JS)	+78 / -4
18 Oct 00:14	`786f5e2`	agent	feat	feat(admin): GraphQL Playground and developer tools in the header; sidebar controls inside the sidebar	+303 / -11
18 Oct 01:19	`b4dd2f0`	owner	chore	chore(config): ignore generated schema and type files	+5 / -0
18 Oct 01:53	`f6d9deb`	agent	feat	feat(admin): header account and cache actions, one sidebar control, themed sidebar icon colours	+529 / -261
18 Oct 02:22	`7787e5d`	agent	feat	feat(admin): run the code generators from the developer tools menu (development only)	+238 / -5
18 Oct 02:44	`6daf209`	agent	feat	feat(admin): restart dev server, create migration and environment-aware developer tools	+538 / -159
18 Oct 03:22	`dab277f`	agent	fix	fix(admin): sidebar group headings keep icons (and collapse) in the rail; remove saved views (query presets)	+94 / -73
18 Oct 03:43	`9f295c8`	agent	fix	fix(admin): responsive layout for phones and tablets (header, dashboard, lists, menus, touch)	+263 / -4

LANDED (LOCAL)	COMMIT	ORIGIN	TYPE	SUBJECT	LINES
18 Oct 06:54	`ff0dd65`	agent	feat	feat(admin): card layout for lists on phones	+227 / -8
18 Oct 06:59	`125225f`	agent	style	style(admin): centre the card checkbox on a media thumbnail	+6 / -0
19 Oct 00:41	`3d2f844`	agent	fix	fix(admin): responsive pass on fonts, menus and touch	+452 / -110
19 Oct 04:07	`d9ba8a3`	agent	refactor	refactor(admin): lay out admin components by Payload slot; UI kit becomes the component gallery	+1,685 / -1,352
19 Oct 04:14	`3aeb9dd`	agent	docs	docs(admin): dashboard integrations research, bundle numbers after the restructure	+121 / -5
19 Oct 04:46	`712a17c`	agent	feat	feat(admin): Site settings sidebar group; Services under Profile	+16 / -13
19 Oct 04:56	`35bea29`	agent	feat	feat(admin): warm off-white canvas for the light theme (ADR 0010)	+85 / -13
19 Oct 05:27	`90807ad`	agent	feat	feat(admin): Roles collection with access levels and capabilities (ADR 0011)	+1,602 / -210
19 Oct 05:47	`1ebcdf5`	agent	feat	feat(admin): GraphQL document tab next to the API tab	+781 / -6
19 Oct 05:50	`c1ec5a8`	agent	fix	fix(admin): trust user-less operations in the last-administrator guards	+26 / -16
19 Oct 05:57	`419dec3`	agent	feat	feat(admin): Site traffic widget (Vercel Web Analytics API)	+805 / -47
19 Oct 06:01	`7dcf315`	agent	feat	feat(admin): Page speed widget (Chrome UX Report field data)	+661 / -2
19 Oct 06:13	`a1fe7c8`	agent	feat	feat(admin): Deployments and CI status widgets	+675 / -7
19 Oct 07:45	`b2a3425`	agent	fix	fix(build): don't fail next build when PAYLOAD_SECRET or POSTGRES_URL is missing	+87 / -1
19 Oct 07:47	`2b7cde3`	agent	fix	fix(admin): rename the RunStatus 'running' tone to 'pending'	+8 / -8
19 Oct 08:00	`1238587`	agent	fix	fix(admin): keep screen-reader text inside truncated widget rows	+7 / -4
19 Oct 21:31	`4dd83a0`	agent	revert	revert: undo the last changes (b2a3425, 2b7cde3, 1238587)	+13 / -102
19 Oct 21:35	`f195abc`	owner	feat	feat(admin): Deployments and CI status widgets	+0 / -0
19 Oct 21:35	`ad48283`	owner	merge	Merge branch 'arena/1e75852c-pocms-payload' of https://github.com/eTarikhi/PoCMS-Payload into arena/admincn/ui	+0 / -0
19 Oct 23:47	`adff4e0`	agent	fix	fix(admin): Page speed widget runs PageSpeed Insights and explains Google errors	+1,346 / -277

F. External references

1. Payload CMS, Drafts: scheduled publish needs a job runner. payloadcms.com/docs/versions/drafts
2. Vercel, Usage and pricing for cron jobs: Hobby allows 100 cron jobs per project, each at most once per day, with per-hour precision. vercel.com/docs/cron-jobs/usage-and-pricing
3. Roadmap baseline: `docs/ui-modernization/shadcn-payload-ui-analysis.md` §8.1 (principles), §9 (phases, estimates, schedule). Bundle history: `docs/ui-modernization/perf-budget.md`. Tools plan: `docs/ui-modernization/dashboard-integrations.md`.
